

INTEGRATED PROGRAM MANAGEMENT REPORT

CDRL A001 · DI-MGMT-81861 · Weekly Submittal

CONTRACT NO.	N40080-22-D-4221	CONTRACT TYPE	Cost-Plus-Incentive-Fee (CPIF)
TITLE	Facility Engineering and Sustainment Support Services		
CONTRACTOR	Meridian Engineering Partners	CEILING	\$11,400,000 (cumulative across base + options)
CURRENT PERIOD	Option Year 2 (06 January 2025 – 05 January 2026)		

Weekly IPMR Summary #105 (OY2 Week 53, Cumulative Week 161 of contract)

Reporting Period: 05 January 2026 – 09 January 2026 · Submitted: 13 January 2026

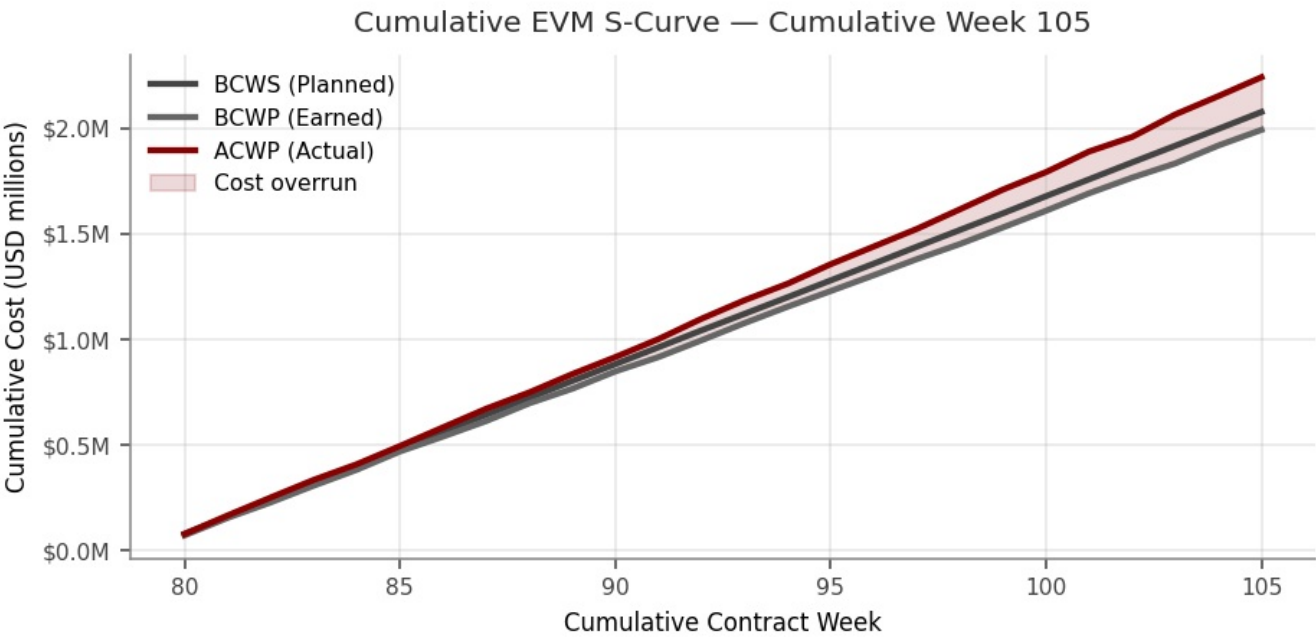


Figure 1. Cumulative EVM S-Curve

Format 1 — Work Breakdown Structure (Cumulative Through 09 January 2026)

WBS Element	BCWS	BCWP	ACWP	CV	SV	EAC
1.1 Engineering Services	\$3,840,000	\$3,710,000	\$4,120,000	-\$410,000	-\$130,000	\$5,310,000
1.2 Inspection & QA	\$2,180,000	\$2,090,000	\$2,275,000	-\$185,000	-\$90,000	\$2,910,000
1.3 Sustainment Planning	\$1,650,000	\$1,540,000	\$1,790,000	-\$250,000	-\$110,000	\$2,140,000
1.4 Program Management	\$890,000	\$885,000	\$963,000	-\$78,000	-\$5,000	\$1,140,000
Total	\$8,560,000	\$8,225,000	\$9,148,000	-\$923,000	-\$335,000	\$11,500,000

CV %: -11.2% | SV %: -3.9% | EAC vs. CBB: \$100K over CBB

Cumulative EVM S-Curve — Cumulative Week 105

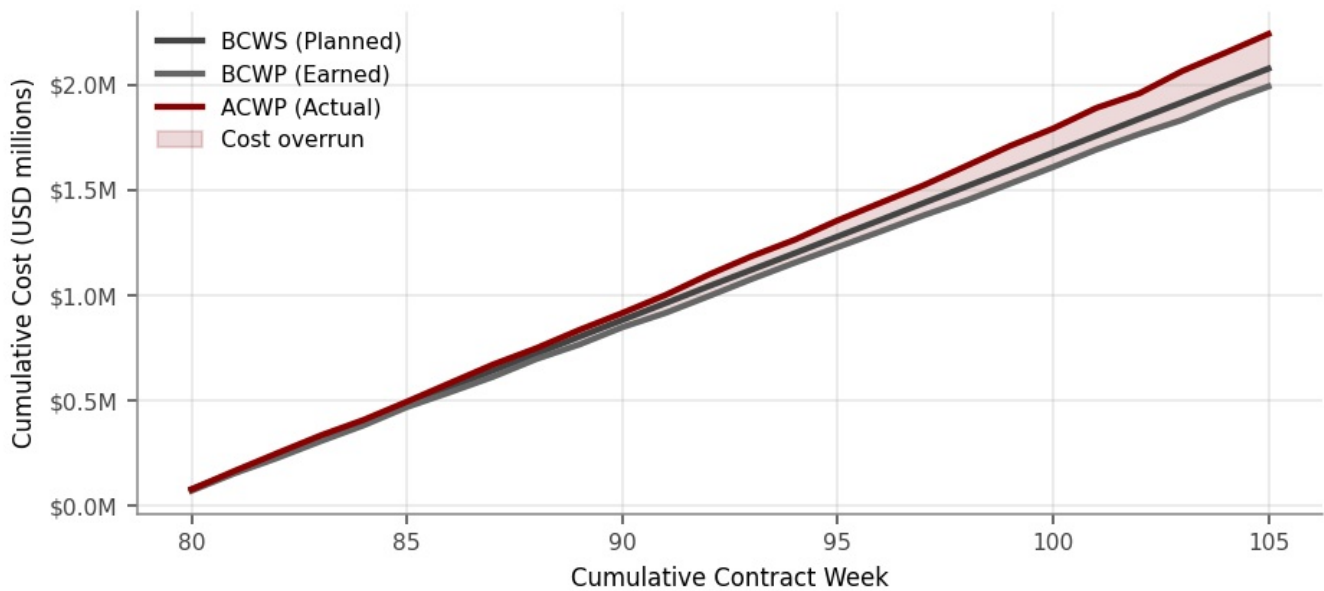


Figure 1. Cumulative EVM S-Curve

Format 5 — Variance Narrative (Excerpts)

WBS 1.1 Engineering Services — Cost Variance Drivers:

- Rework on Hangar 405 mechanical systems analysis (May–July 2025): \$187K. Original analysis directed verbally in April 2025 by NAS Pax River Public Works Officer (Mr. Becker) using legacy facility data. Analysis was completed in June 2025; in July, written COR direction superseded the original tasking and required re-analysis using current as-built drawings. (*See Weekly Reports #28–35 for chronology.*)
- Scope expansion of Pier 6 structural assessment (Q3 OY1): \$142K. Initial scope verbally expanded by Capt. Mark Walsh (Installation Operations) during a site visit; subsequent COR direction required documenting and re-baselining the expanded scope, resulting in re-work of preliminary findings.
- Continued tier-2 engineering support for tenant command requests outside published portfolio backlog: ~\$80K cumulative.

WBS 1.3 Sustainment Planning — Cost Variance Drivers:

- Rework on Building 1102 facility condition assessment (Q4 OY1): \$116K. Mr. Becker had directed Meridian to use a 30-year planning horizon during a verbal coordination meeting in October 2025. COR subsequently directed in December 2025 that the planning horizon should be 50 years per current SECNAVINST guidance. Assessment required regeneration of life-cycle cost models.

WBS-Level Variance Distribution — Wk 105

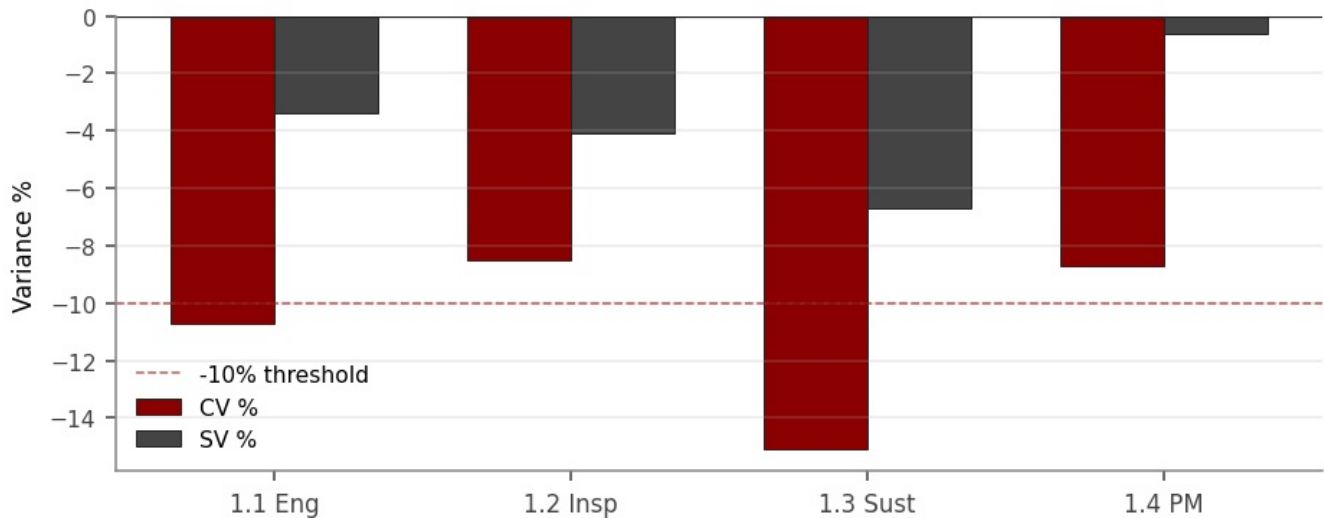


Figure 2. WBS-Level Variance Distribution

Issues, Risks, and RFIs

Open RFIs at start of reporting period:

- RFI-088 (submitted 19 December 2025, OY2 Week 50): Clarification on PWS Section 5.2 — scope of "engineering technical support" for tenant command-controlled facilities (specifically NAVAIR test facilities). 21 days open.
- RFI-089 (submitted 22 December 2025): Authority to commit subcontractor labor for Pier 6 structural assessment continuation. 18 days open.
- RFI-091 (submitted 30 December 2025): Clarification on PWS Section 6.1 — deliverable format for facility condition assessments (DD Form 1391-style vs. NAVFAC P-78 format). 10 days open.

RFIs submitted this period:

- **RFI-092 (submitted 08 January 2026):** Mr. Becker (PWO) has informally requested Meridian to prepare a "rough order of magnitude" cost estimate for converting Building 1145 to flexible office space. Meridian has not begun work pending COR direction. Request COR confirmation that this task falls within current PWS scope or requires task order modification. *Status: Open.*

Pending Items / Government Action Required

- Four (4) RFIs open.
- REA narrative for Hangar 405 rework (originally identified in OY1 Week 32) is in pre-submission review with Meridian contracts staff.
