

INTEGRATED PROGRAM MANAGEMENT REPORT

CDRL A001 · DI-MGMT-81861 · Weekly Submittal

CONTRACT NO.	N40080-22-D-4221	CONTRACT TYPE	Cost-Plus-Incentive-Fee (CPIF)
TITLE	Facility Engineering and Sustainment Support Services		
CONTRACTOR	Meridian Engineering Partners	CEILING	\$11,400,000 (cumulative across base + options)
CURRENT PERIOD	Option Year 2 (06 January 2025 – 05 January 2026)		

Weekly IPMR Summary #107 (OY2 Week 55, Cumulative Week 163)

Reporting Period: 19 January 2026 – 23 January 2026 · Submitted: 27 January 2026

Format 1 — WBS Cumulative

CV cumulative: -\$967K (-11.5%). SV cumulative: -\$361K. EAC: \$11,560,000.

Work Accomplished This Period

- Received written COR response on 21 January 2026 closing RFI-088: Engineering technical support for NAVAIR test facilities is **NOT** in PWS scope unless directed via written task assignment from COR. Any tenant command requests for this support shall be referred to the COR for evaluation and possible separate procurement.
- Received written COR response on 22 January 2026 closing RFI-089: Subcontractor labor for Pier 6 close-out is authorized within current task order ceiling.
- Issued internal communication to Meridian engineering team on revised PWS interpretation per RFI-088 closure.
- Capt. Walsh contacted Meridian PM Voss directly on 22 January 2026 regarding RFI-088 closure. Capt. Walsh expressed concern that NAVAIR test facility support has been "informally provided" since the original contract award and that the COR's interpretation represents a scope reduction. Meridian advised Capt. Walsh that the COR's written direction is controlling and that any disagreement should be raised by Capt. Walsh's office directly with the COR or KO.

Issues, Risks, and RFIs

- RFI-094 (submitted 23 January 2026):** Following RFI-088 closure and direct contact from Capt. Walsh, request COR direction on disposition of approximately 340 hours of NAVAIR test facility engineering support performed by Meridian during OY1 and OY2 to date (estimated value \$87K). Same pattern as Cardinal's after-hours support situation: prior contractor action under unclear scope direction, retroactively determined out-of-scope. *Status: Open.*
- RFI-091, RFI-092, RFI-093 remain open. RFI-088 closed after 35 days. RFI-089 closed after 32 days.

Pending Items / Government Action Required

- Four (4) RFIs open.
- REA submission for Hangar 405 rework now scheduled for Week 56.

Estimate at Completion (EAC) — Trend Through Wk 107

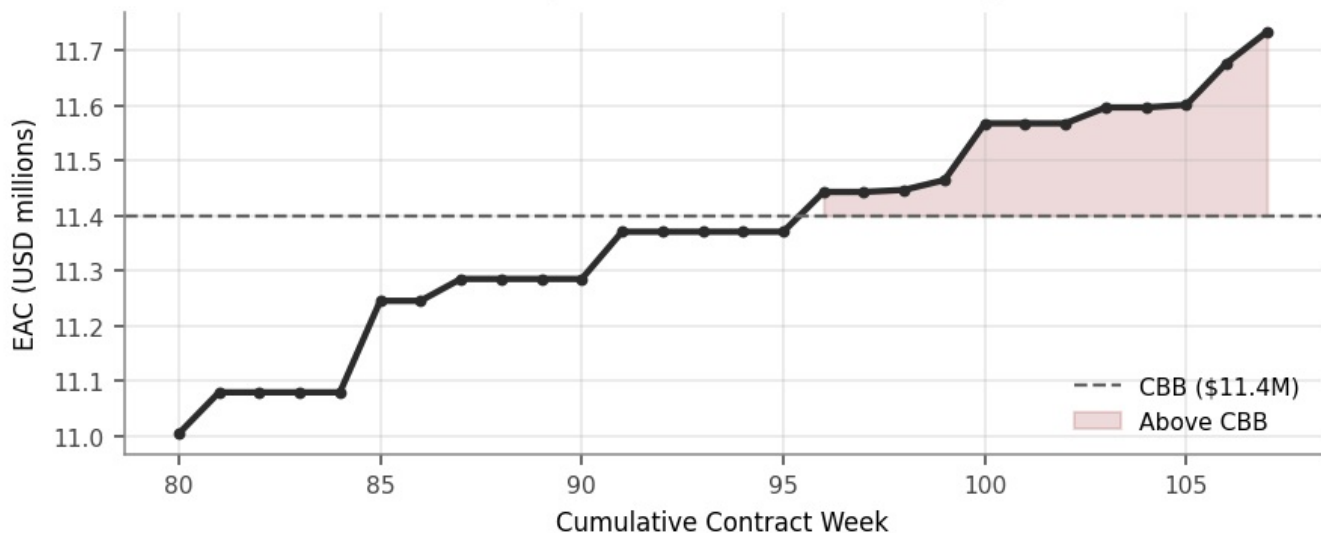


Figure 3. EAC Trend Through Reporting Period
