

INTEGRATED PROGRAM MANAGEMENT REPORT

CDRL A001 · DI-MGMT-81861 · Weekly Submittal

CONTRACT NO.	N40080-22-D-4221	CONTRACT TYPE	Cost-Plus-Incentive-Fee (CPIF)
TITLE	Facility Engineering and Sustainment Support Services		
CONTRACTOR	Meridian Engineering Partners	CEILING	\$11,400,000 (cumulative across base + options)
CURRENT PERIOD	Option Year 2 (06 January 2025 – 05 January 2026)		

Weekly IPMR Summary #109 (OY2 Week 57, Cumulative Week 165)

Reporting Period: 02 February 2026 – 06 February 2026 · Submitted: 10 February 2026

Format 1 — WBS Cumulative

CV cumulative: -\$1,062,000 (-12.4%). SV cumulative: -\$401K. EAC: \$11,690,000.

Work Accomplished This Period

- Received written COR response on 04 February 2026 closing RFI-092 (Building 1145 conversion estimate): Task **NOT** authorized at this time. Future task order may address. RFI-092 closed after 27 days.
- Received written COR response on 05 February 2026 closing RFI-093 (PWS 3.4 interpretation): "As directed" within PWS Section 3.4 means **direction issued in writing by the COR**. Verbal or informal direction from tenant command stakeholders is not authoritative. Meridian shall reject any non-COR direction.
- Drafted internal communication packaging RFI-093 closure for Meridian engineering team.
- Initiated cost segregation exercise to identify which NAVAIR test facility support hours were performed against verbal vs. inferred direction (RFI-094 supporting analysis).

Issues, Risks, and RFIs

- RFI-094 remains open (now 14 days).
- No new RFIs this period.**
- Variance attribution analysis (per Meridian internal QA):** Of cumulative \$1.062M cost variance through week 57 of OY2, Meridian estimates approximately:
 - \$445K (42%) attributable to documented rework events (Hangar 405, Pier 6, Building 1102) — *all three traceable to verbal-vs-written direction conflicts*
 - \$87K (8%) pending RFI-094 disposition (NAVAIR test facility support)
 - \$230K (22%) attributable to scope ambiguity in PWS Sections 3.4, 5.2, 6.1
 - Remaining \$300K (28%) attributable to various factors including labor escalation, subcontractor cost variance, and standard programmatic variance

Approximately 50–70% of cumulative cost variance is traceable to government-side scope and direction ambiguity, not to contractor performance.

Pending Items / Government Action Required

- One (1) RFI open.
- REA disposition pending KO action.

Estimate at Completion (EAC) — Trend Through Wk 109

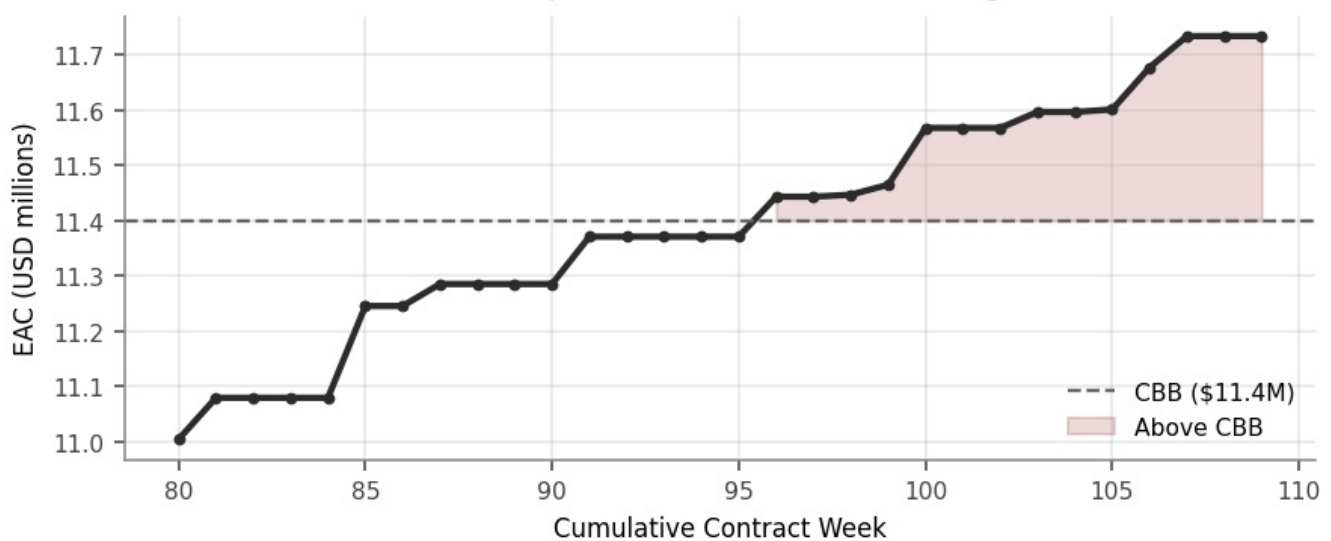


Figure 3. EAC Trend Through Reporting Period

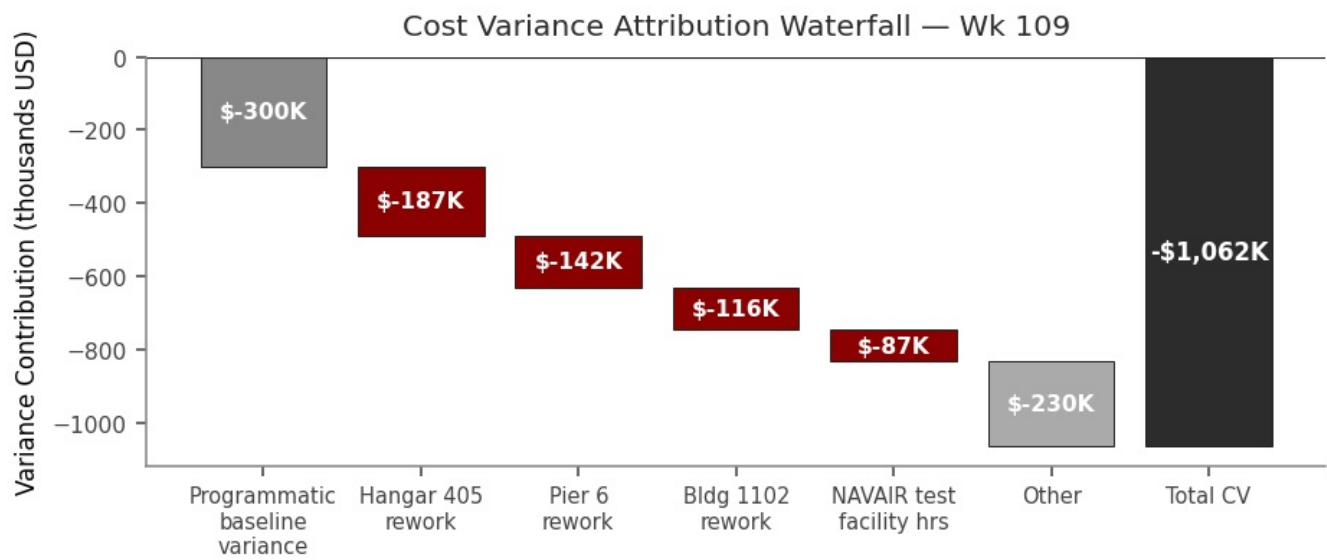


Figure 4. Cost Variance Attribution Waterfall
