

CONTRACT		
N40080-25-D-5318	TYPE Cost-Plus-Fixed-Fee (CPFF)	CEILING \$5,400,000
TITLE		
Energy Audit and Optimization Support Services		

Weekly Status Report #28

12 January 2026 – 16 January 2026 · Submitted 19 January 2026 · 28 of 52 (Base Year)

1. Work Accomplished This Period

- Received COR comments on Q1 utility benchmarking report on 13 January 2026 (5-day turnaround). Comments incorporated; revised report submitted 16 January 2026.
- Completed Building 2118 energy audit data analysis. Draft report in internal QA review.
- Initiated Building 2218 ASHRAE Level II audit fieldwork. Site walkthrough completed; instrumentation deployment in progress.

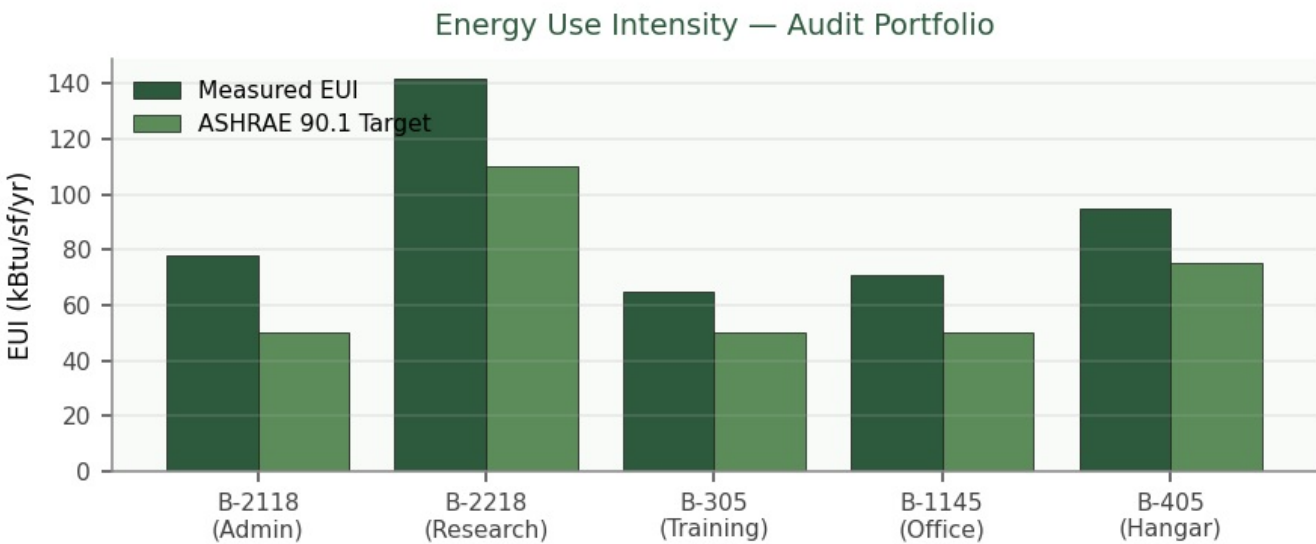


Figure 1. Energy Use Intensity — Audit Portfolio Buildings

2. Work Planned Next Period

- Submit Building 2118 audit report to COR.
- Continue Building 2218 fieldwork (target completion: end of week 30).

3. Issues, Risks, and RFIs

- RFI-014 (submitted 14 January 2026):** Building 2218 is partially occupied by NAVAIR Test Range Engineering tenant operations. Request COR confirmation that audit may proceed with limited access to two Test Range-controlled rooms. *Status: Open.*

4. Cost and Schedule Performance

CV cumulative: -\$41K (-1.5%). SV cumulative: -\$22K. EAC: \$5,460,000. No material change.

5. Pending Items / Government Action Required

- One (1) RFI open (submitted today).

ASHRAE Level II Audit Portfolio — Status as of Wk 28

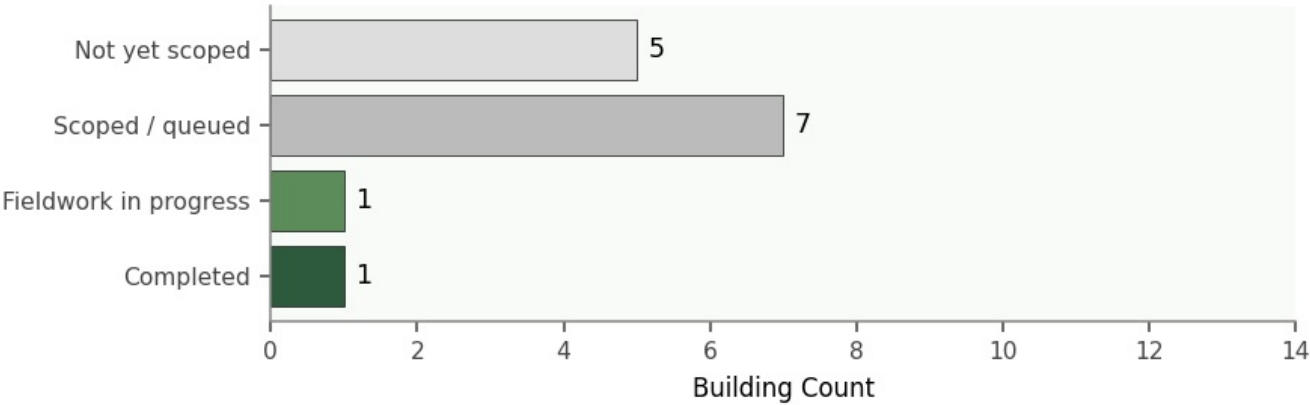


Figure 2. Audit Portfolio Status — Wk 28 Update
