

INTEGRATED PROGRAM MANAGEMENT REPORT

CDRL A001 · DI-MGMT-81861 · Weekly Submittal

CONTRACT NO.	N40080-22-D-4221	CONTRACT TYPE	Cost-Plus-Incentive-Fee (CPIF)
TITLE	Facility Engineering and Sustainment Support Services		
CONTRACTOR	Meridian Engineering Partners	CEILING	\$11,400,000 (cumulative across base + options)
CURRENT PERIOD	Option Year 2 (06 January 2025 – 05 January 2026)		

Weekly IPMR Summary #106 (OY2 Week 54, Cumulative Week 162)

Reporting Period: 12 January 2026 – 16 January 2026 · Submitted: 20 January 2026

Cumulative EVM S-Curve — Cumulative Week 106

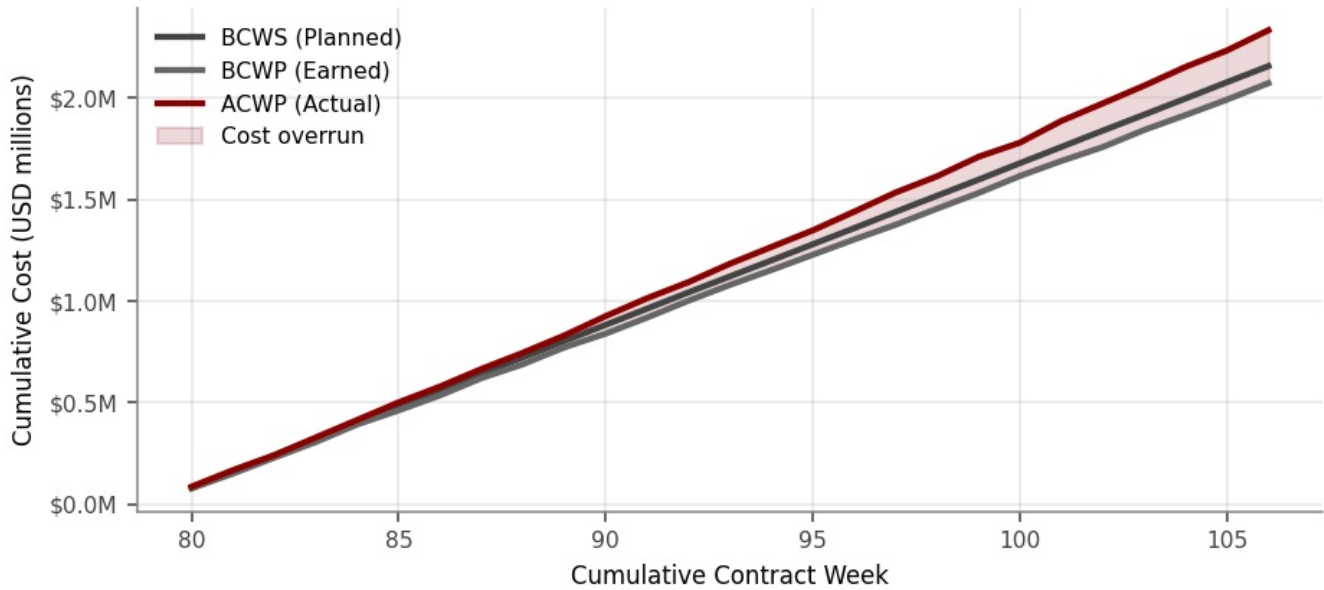


Figure 1. Cumulative EVM S-Curve

Format 1 — WBS Cumulative

CV cumulative: -\$948K (-11.4%). SV cumulative: -\$352K. EAC: \$11,540,000.

Format 5 — Variance Narrative (Selected Excerpts)

This-period drivers:

- Engineering Services labor surge to support Pier 6 close-out (delayed deliverable): \$42K above baseline. Driver: continued reconciliation of verbal vs. written scope direction received during Q3 OY1.
- No new significant variance events this period.

Work Accomplished This Period

- Submitted draft Hangar 405 mechanical systems re-analysis to COR for review (deliverable was on revised baseline).
- Continued Pier 6 structural assessment close-out documentation.
- Initiated facility condition assessment fieldwork for Buildings 230 and 233 (next portfolio increment).
- Met with Mr. Becker (PWO) on 14 January 2026. Mr. Becker reiterated interest in Building 1145 conversion estimate (RFI-092). Meridian advised RFI-092 remained pending COR response and that no work would be performed.

Issues, Risks, and RFIs

- RFI-093 (submitted 16 January 2026):** PWS Section 3.4 references Meridian providing "engineering support to tenant commands as directed." Request COR clarification on the meaning of "as directed" — by whom and through what channel. Meridian has historically interpreted this to mean direction issued by the COR; recent stakeholder requests (RFI-092 Building 1145, prior verbal direction from Capt. Walsh on Pier 6) suggest tenant commands believe they may direct under this clause. *Status: Open.*
- RFI-088, RFI-089, RFI-091, RFI-092 remain open.

Pending Items / Government Action Required

- Five (5) RFIs open.
- RFI-088 now 28 days open.

