

INTEGRATED PROGRAM MANAGEMENT REPORT

CDRL A001 · DI-MGMT-81861 · Weekly Submittal

CONTRACT NO.	N40080-22-D-4221	CONTRACT TYPE	Cost-Plus-Incentive-Fee (CPIF)
TITLE	Facility Engineering and Sustainment Support Services		
CONTRACTOR	Meridian Engineering Partners	CEILING	\$11,400,000 (cumulative across base + options)
CURRENT PERIOD	Option Year 2 (06 January 2025 – 05 January 2026)		

Weekly IPMR Summary #108 (OY2 Week 56, Cumulative Week 164)

Reporting Period: 26 January 2026 – 30 January 2026 · Submitted: 03 February 2026

Cumulative EVM S-Curve — Cumulative Week 108

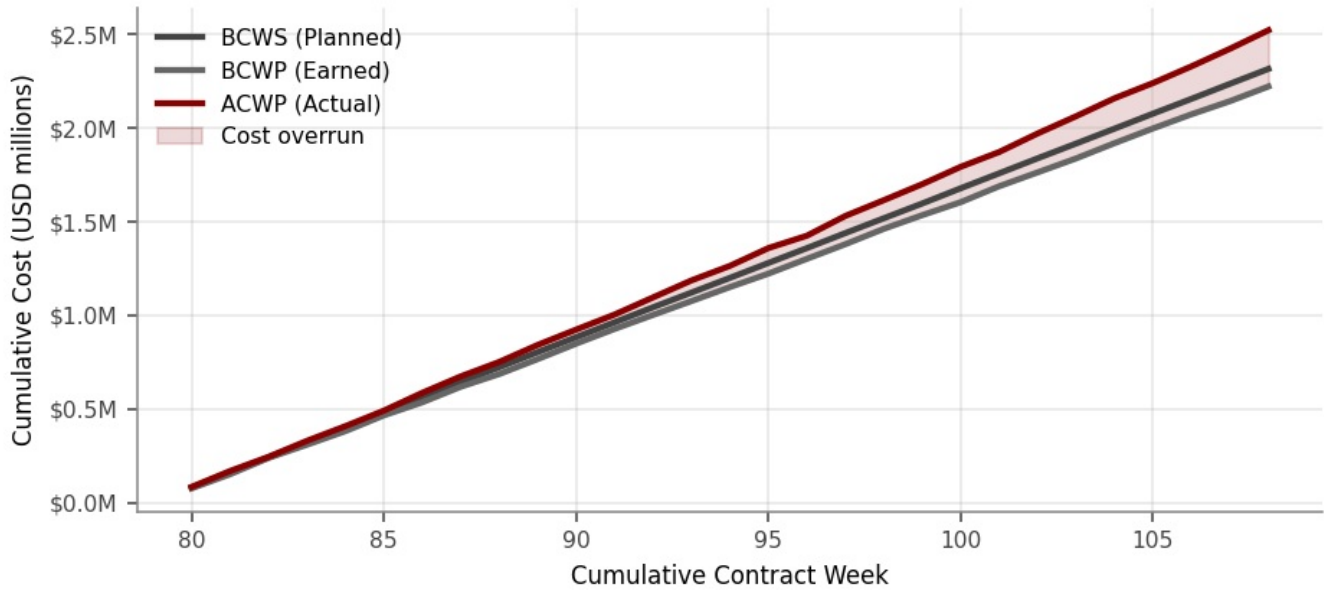


Figure 1. Cumulative EVM S-Curve

Format 1 — WBS Cumulative

CV cumulative: -\$1,031,000 (-12.1%). SV cumulative: -\$389K. EAC: \$11,640,000.

Format 5 — Variance Narrative (Selected Excerpts)

This-period variance drivers:

- WBS 1.1 Engineering Services: Additional \$52K in unfavorable cost variance recognized this period as Meridian completed disposition of NAVAIR test facility support hours per RFI-094 disposition (pending). Costs previously held in suspense are now reflected in ACWP.

Work Accomplished This Period

- Submitted formal REA package to KO on 28 January 2026 covering: (a) Hangar 405 mechanical re-analysis rework (\$187K), (b) Pier 6 scope expansion rework (\$142K), (c) Building 1102 planning-horizon rework (\$116K). Total REA: \$445K plus indirect.
- Received written COR response on 29 January 2026 on RFI-091: Facility condition assessments shall use NAVFAC P-78 format. RFI-091 closed after 30 days.
- Continued FCA fieldwork on Buildings 230, 233.

Issues, Risks, and RFIs

- No new RFIs this period.
- RFI-092, RFI-093, RFI-094 remain open.

Pending Items / Government Action Required

- Three (3) RFIs open.
- REA disposition needed.

Estimate at Completion (EAC) — Trend Through Wk 108

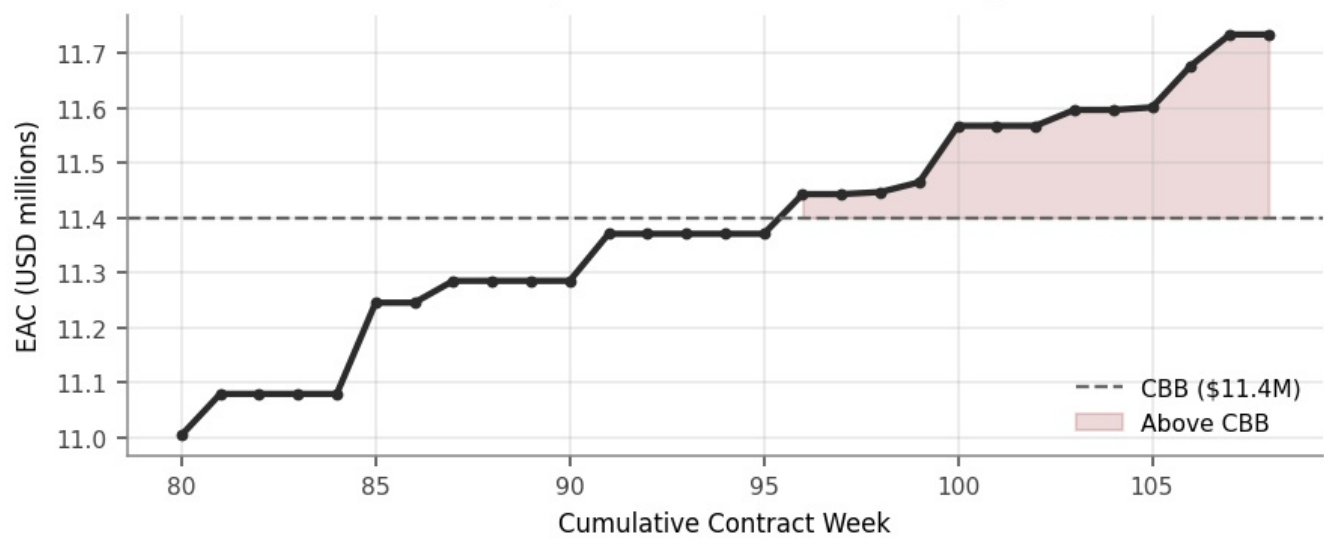


Figure 3. EAC Trend Through Reporting Period
