

DEPARTMENT OF THE NAVY
NAVAL FACILITIES ENGINEERING SYSTEMS COMMAND ATLANTIC

CDRL Submittal per DD Form 1423-1 — Weekly Status Report

DISTRIBUTION STATEMENT A — APPROVED FOR PUBLIC RELEASE; DISTRIBUTION IS UNLIMITED

Contract Number: N40080-24-D-1042
Contract Title: Environmental Compliance and Permitting Support Services
Contractor: Atlantic Environmental Solutions, LLC
Contract Type: IDIQ with FFP Task Orders
Period of Performance: 05 January 2026 – 04 January 2027 (12 months)
CDRL: A001 — Weekly Status Report per DD Form 1423-1 (DI-MGMT-80368A)
COR: Mr. James Hollister, NAVFAC Atlantic NAS Patuxent River PWD Services Branch

Weekly Status Report #4

Reporting Period: 26 January 2026 – 30 January 2026 **Submission Date:** 02 February 2026 **Contract Week:** 4 of 52 (Base Year)

1. WORK ACCOMPLISHED THIS PERIOD

- Completed inspections of 8 additional USTs (cumulative: 12 of 14 originally-scoped tanks).
- Drafted UST inspection summary reports for 4 tanks; in internal QA review.
- Received written response from COR (Mr. Hollister) on 28 January 2026 addressing RFI-001 and RFI-002:
- RFI-001 response:** NAVAIR PMA-265 support is **NOT** in scope under base contract; separate task order required.
- RFI-002 response:** All technical direction must be issued in writing through the COR. Verbal guidance from tenant command POCs is non-binding.

2. WORK PLANNED NEXT PERIOD

- Complete remaining 2 originally-scoped UST inspections.
- Hold internal stand-down to communicate written direction policy to contractor staff.

3. ISSUES, CONCERNS, AND RFIS SUBMITTED

- RFI-006 (submitted 30 January 2026):** Following COR response to RFI-002, request guidance on how to handle outstanding informal direction received from LCDR Reyes (RFI-003 expanded UST scope) and Ms. Murphy (RFI-005 PMA-265 support). Contractor has not performed work against either set of informal direction but seeks formal closure. *Status: Open.*
- RFI-003, RFI-004, RFI-005 remain open. RFI-001, RFI-002 closed.

Open RFI Age — End of Week 4

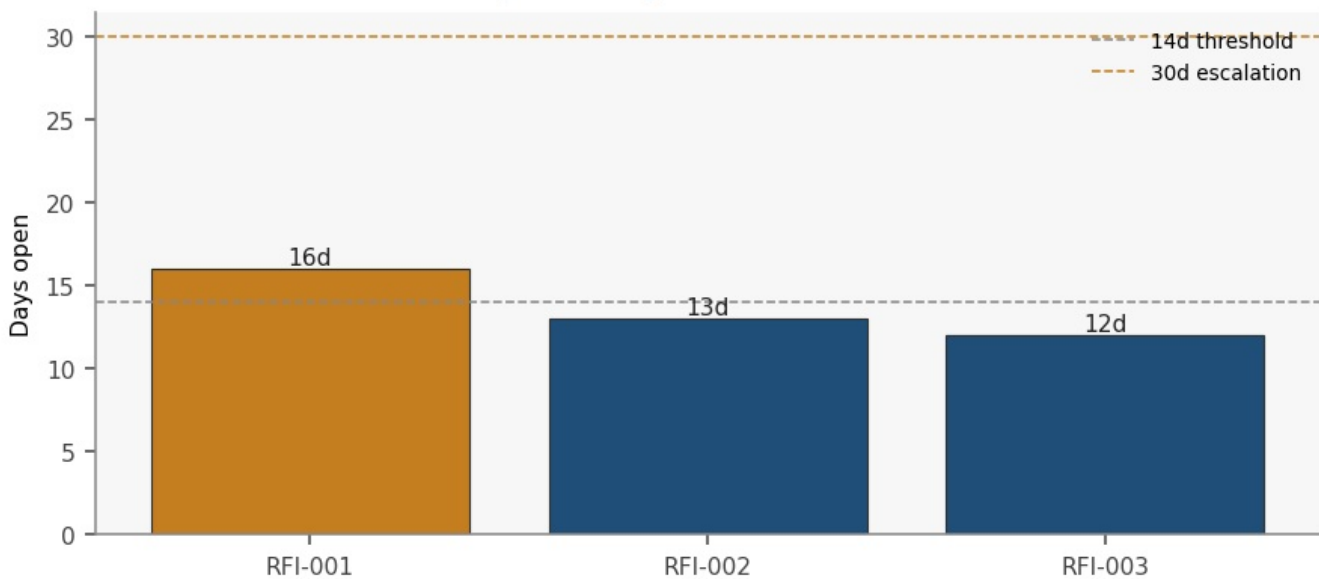


Figure 2. Open RFI Age — RFI-004 Approaching 14-Day Threshold

4. COST AND SCHEDULE STATUS

TO 0001: Schedule slip of approximately 5 days projected against original permit submission milestone due to RFI-004 delay (still open at 16 days). TO 0002: On schedule for original 14-tank scope.

5. PENDING ITEMS / GOVERNMENT ACTION REQUIRED

-
- Four (4) RFIs open. RFI-004 (16 days) is critical path.
 - Contractor requests written confirmation from COR that no fee or scope adjustment is required for time spent on inspections subsequently determined to be out of scope.

Submitted by:

Sarah Chen, PMP, Contractor Project Manager

Date: 02 February 2026
