

INTEGRATED PROGRAM MANAGEMENT REPORT

CDRL A001 · DI-MGMT-81861 · Weekly Submittal

CONTRACT NO.	N40080-22-D-4221	CONTRACT TYPE	Cost-Plus-Incentive-Fee (CPIF)
TITLE	Facility Engineering and Sustainment Support Services		
CONTRACTOR	Meridian Engineering Partners	CEILING	\$11,400,000 (cumulative across base + options)
CURRENT PERIOD	Option Year 2 (06 January 2025 – 05 January 2026)		

Weekly IPMR Summary #110 (OY2 Week 58, Cumulative Week 166)

Reporting Period: 09 February 2026 – 13 February 2026 · Submitted: 17 February 2026

Cumulative EVM S-Curve — Cumulative Week 110

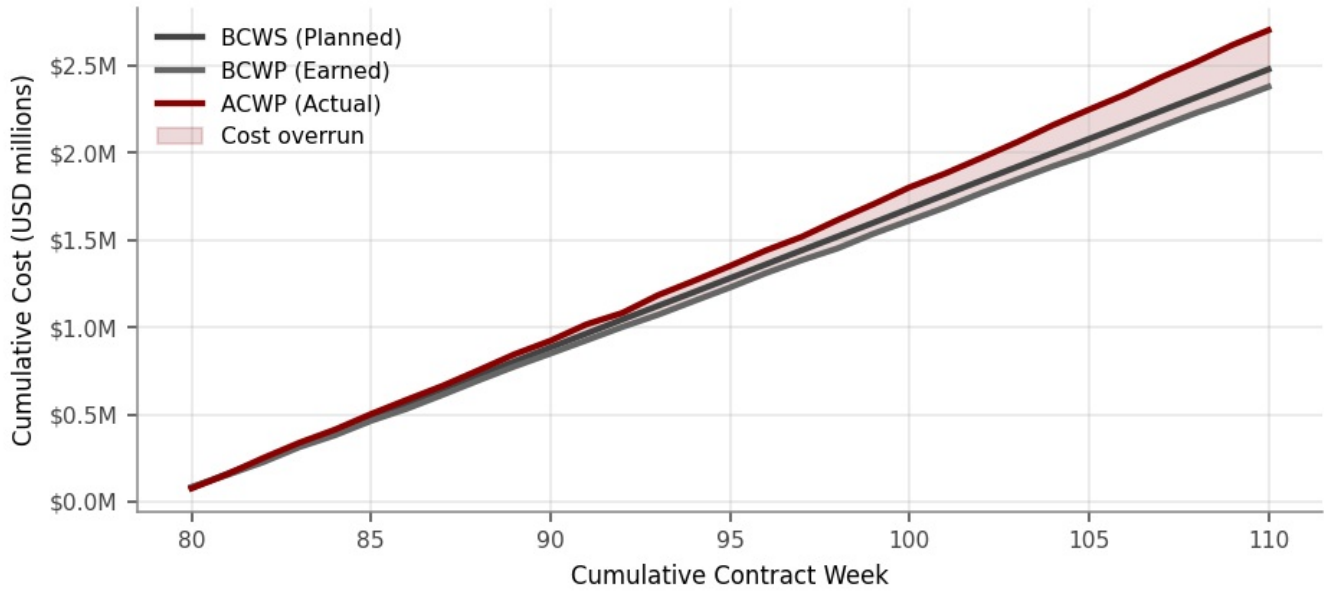


Figure 1. Cumulative EVM S-Curve

Format 1 — WBS Cumulative (Final OY2 Window)

WBS Element	BCWS	BCWP	ACWP	CV	SV	EAC
1.1 Engineering Services	\$4,012,000	\$3,872,000	\$4,389,000	-\$517,000	-\$140,000	\$5,420,000
1.2 Inspection & QA	\$2,266,000	\$2,184,000	\$2,401,000	-\$217,000	-\$82,000	\$2,990,000
1.3 Sustainment Planning	\$1,720,000	\$1,608,000	\$1,879,000	-\$271,000	-\$112,000	\$2,200,000
1.4 Program Management	\$928,000	\$922,000	\$1,012,000	-\$90,000	-\$6,000	\$1,180,000
Total	\$8,926,000	\$8,586,000	\$9,681,000	-\$1,095,000	-\$340,000	\$11,790,000

CV %: -12.6% | SV %: -3.8% | EAC vs. CBB: \$390K over CBB | Trend: Adverse, stabilizing

Work Accomplished This Period

- Continued FCA fieldwork on Buildings 230, 233. Drafts in preparation.
- Submitted RFI-094 supporting analysis to COR (NAVAIR test facility support cost segregation).
- Received KO acknowledgment of REA package; review timeline indicated as 30–45 days.
- Held PMR (Program Management Review) with COR Hollister and KO Tan on 11 February 2026. Topics covered:
- Cost variance trajectory and primary drivers (rework events).
- Status of pending REA.
- Open RFIs and resolution cadence.
- Forward strategy for OY3 (decision pending in Q3 FY26).

Issues, Risks, and RFIs

- RFI-095 (submitted 12 February 2026):** Following PMR discussion of OY3 decision, request COR guidance on whether Meridian should begin OY3 mobilization planning or assume probable non-exercise. *Status: Open.*
- RFI-094 remains open (now 21 days).

Cumulative RFI Metrics (Cumulative Through Week 58 of OY2 / Cumulative Week 166)

- Cumulative RFIs submitted (contract life-to-date): 92
- Cumulative RFIs answered: 71

- Currently open: 21 (5 currently >30 days)
- **Average COR response time: 31 days**
- **Verbal-vs-written direction conflicts producing rework: 3 documented events** (Hangar 405, Pier 6, Building 1102)
- **Total cost variance attributable to rework events: \$445,000**

Variance Summary (PNR-Style)

Cumulative cost variance on this contract has grown from approximately -3% at end of OY1 Q1 to -12.6% currently. The trajectory of cost variance has tracked closely with two contract administration metrics:

(1) Cumulative count of open RFIs (correlation $r \approx 0.74$ across OY1 and OY2) (2) Cumulative count of documented verbal-vs-written direction conflicts (3 conflicts; each followed by measurable cost variance growth in subsequent weeks)

Contractor performance metrics (deliverable acceptance rate, rework on contractor-internal QA, schedule performance against revised baselines) remain within acceptable bounds.

The contractor recommends — for inclusion in the eventual CPARS narrative and for application to follow-on procurements — that the program office assess:

- COR span of control (Mr. Hollister currently CORs four concurrent services contracts at NAS Patuxent River PWD per common knowledge).
- Formal change control / written-only direction policy.
- PWS language standardization for tenant command coordination and "as directed" clauses.

End of Weekly IPMR Summaries for Reporting Window Q1 FY26.

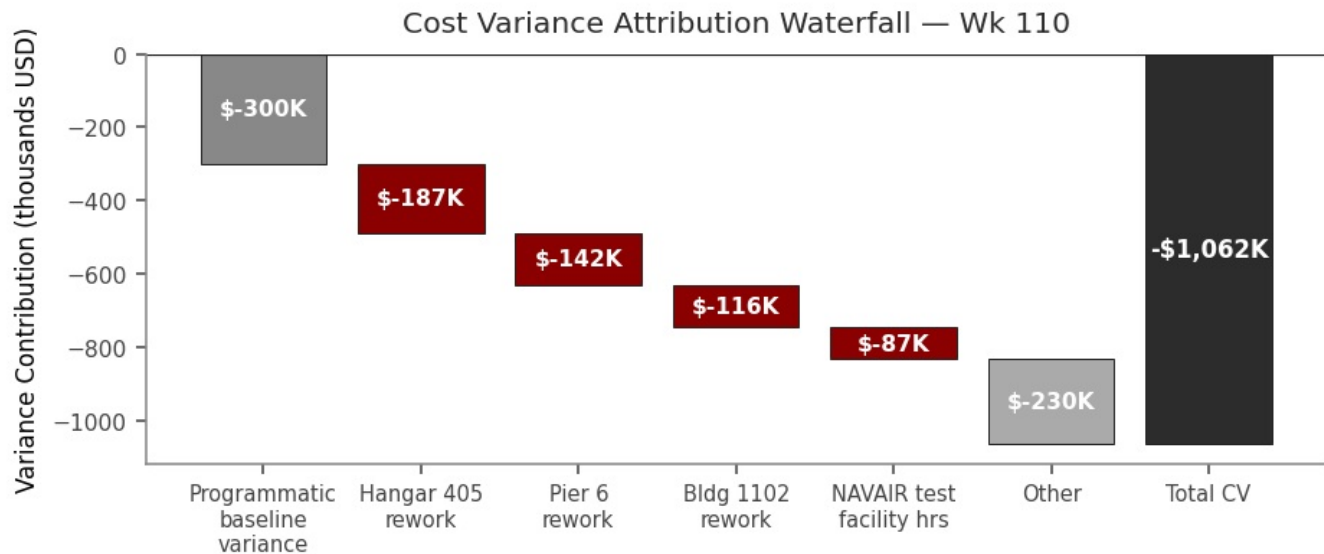


Figure 4. Cost Variance Attribution Waterfall

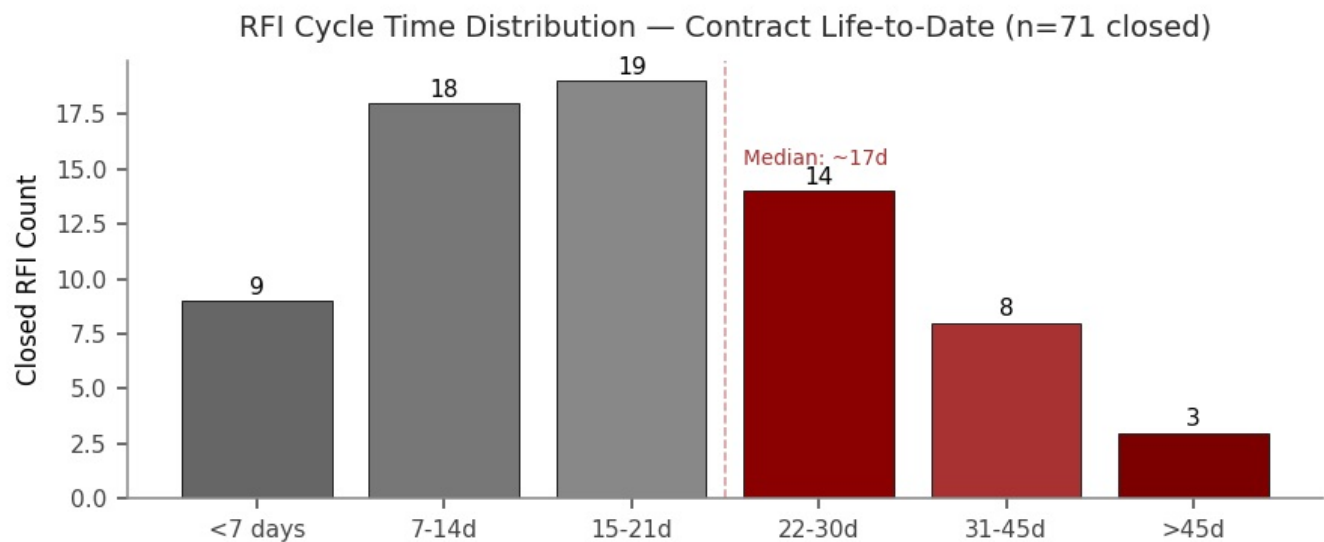


Figure 5. RFI Cycle Time Distribution — Contract Life-to-Date
