

Contract: N40080-23-D-3155 · Service: Installation IT Help Desk and Tier 2 Support Services · Type: Cost-Plus-Fixed-Fee (CPFF)

Weekly Status Report #58 (OY1 Week 57, Cumulative Week 110)

Reporting Period: 09 February 2026 – 13 February 2026 · Submitted: 16 February 2026

TIER 1 ATA 8m 24s ▲ Within target	TIER 2 ATR 4.9d ▲ Within target	OPEN QUEUE 169 ▼ -9 vs LW	P1 SLA 7/7 100%
--	--	--	------------------------------

1. OPERATIONAL SUMMARY

- Tickets opened: 471. Closed: 480. Net open queue: 169 (down 9).
- Tier 1 ATA: 8 min 24 sec.
- Tier 2 ATR: 4.9 days.
- Priority-1 incidents: 7; all within SLA.

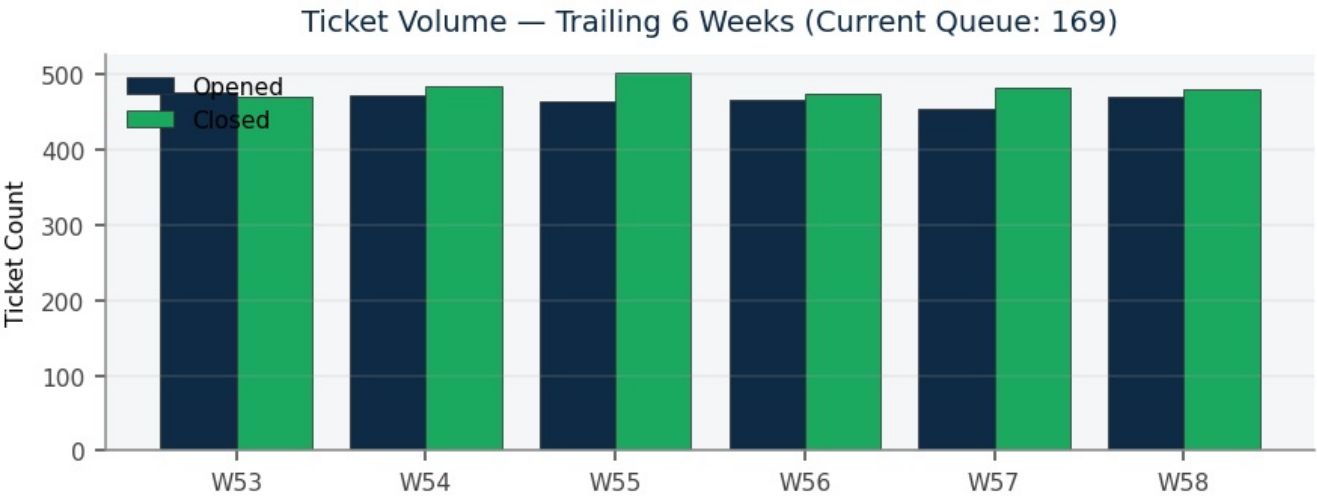


Figure 1. Ticket Volume — 6-Week Trailing

2. WORK ACCOMPLISHED

- Account migration: 84 accounts (cumulative 1,409 of approximately 2,200).
- Received COR response 11 February 2026 closing RFI-042 (KVM procurement authority): Approved, with stipulation that procurement be coordinated with installation supply per existing process. RFI-042 closed after 62 days.
- Received COR response 11 February 2026 on RFI-044 (software deployment approval workflow): COR will issue revised workflow within 30 days. Interim guidance: route all non-standard software requests through COR for individual approval. RFI-044 closed after 51 days.

3. ISSUES, RISKS, AND RFIS

- RFI-050 (submitted 12 February 2026):** Reference RFI-044 interim guidance. Cardinal currently has a backlog of 7 non-standard software requests submitted by tenant command users since November. Request prioritization guidance from COR for processing the backlog. *Status: Open.*
- RFI-048 (REA disposition), RFI-049 remain open.

4. COST AND SCHEDULE PERFORMANCE (CUMULATIVE THROUGH OY1 WEEK 57)

Metric	Value
BCWS Cumulative	\$5,318,000
BCWP Cumulative	\$5,224,000
ACWP Cumulative	\$5,663,000
CV	-\$439,000
CV %	-8.4%
EAC	\$6,920,000

5. CUMULATIVE RFI METRICS THROUGH WEEK 57 OF OY1

- Cumulative RFIs submitted: 47
- Cumulative RFIs answered: 33
- Currently open: 14 (3 currently >30 days old)
- **Average COR response time: 26 days**
- **Longest closed-out RFI cycle: RFI-042 at 62 days**

6. CONTRACTOR COMMENTS

Cardinal observes that cost variance against this contract has tracked closely with the cumulative volume of open RFIs over the last two quarters. Two specific events — the ENGAGE platform rework and the after-hours support scope ambiguity — together account for approximately \$195K of the current \$441K cumulative cost variance. Both events share the same proximate cause: contractor action against informal/verbal direction from non-COR personnel, subsequently superseded by written COR direction. Cardinal has implemented internal policy requiring written COR confirmation before action on any non-COR direction. Cardinal recommends that the program office consider formalizing a written-only direction policy at the program office level as a preventive measure for the broader services portfolio.

End of Weekly Status Reports for Reporting Window Q1 FY26.

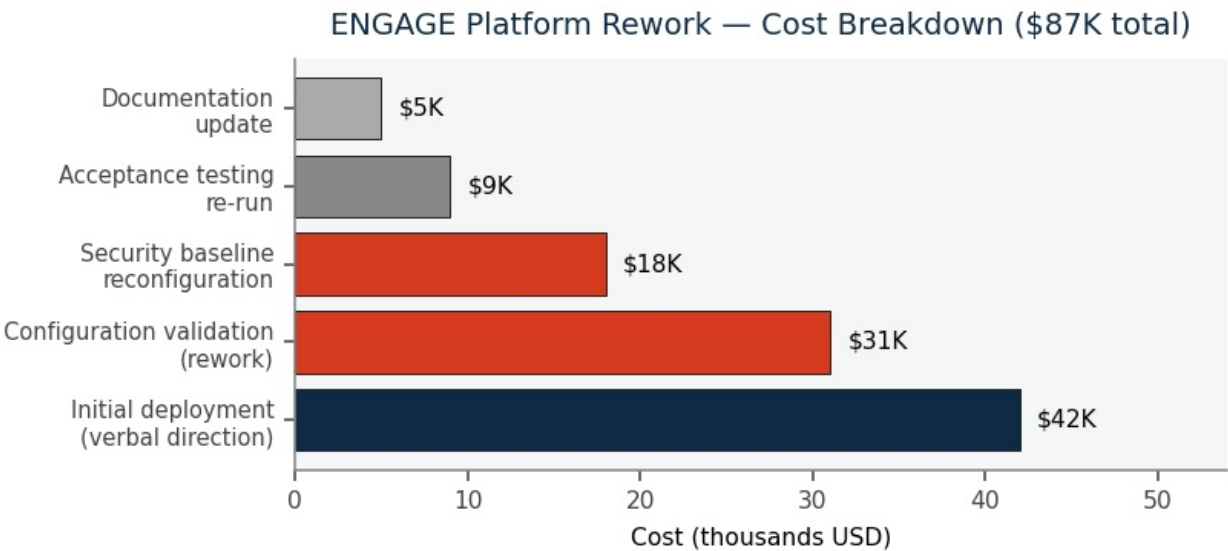


Figure 2. ENGAGE Platform Rework — Cost Attribution
