

Contract: N40080-23-D-3155 · Service: Installation IT Help Desk and Tier 2 Support Services · Type: Cost-Plus-Fixed-Fee (CPFF)

Weekly Status Report #53 (OY1 Week 52, Cumulative Week 105 of contract)

Reporting Period: 05 January 2026 – 09 January 2026 · Submitted: 12 January 2026

TIER 1 ATA 8m 14s ▲ Within target	TIER 2 ATR 4.7d ▲ Within target	OPEN QUEUE 156 ▼ -25 vs LW	P1 SLA 11/11 100%
--	--	---	--------------------------------

1. OPERATIONAL SUMMARY

- Tickets opened this period: 487. Closed: 462. Net open queue at end of period: 156 (down 25).
- Tier 1 average time-to-acknowledge: 8 min 14 sec (target ≤ 10 min).
- Tier 2 average time-to-resolve: 4.7 days (target ≤ 5.0 days, however tier 2 metric has trended upward over option year — see comments).
- 11 priority-1 incidents handled; 11 closed within 4-hour SLA.

Ticket Volume — Trailing 6 Weeks (Current Queue: 156)

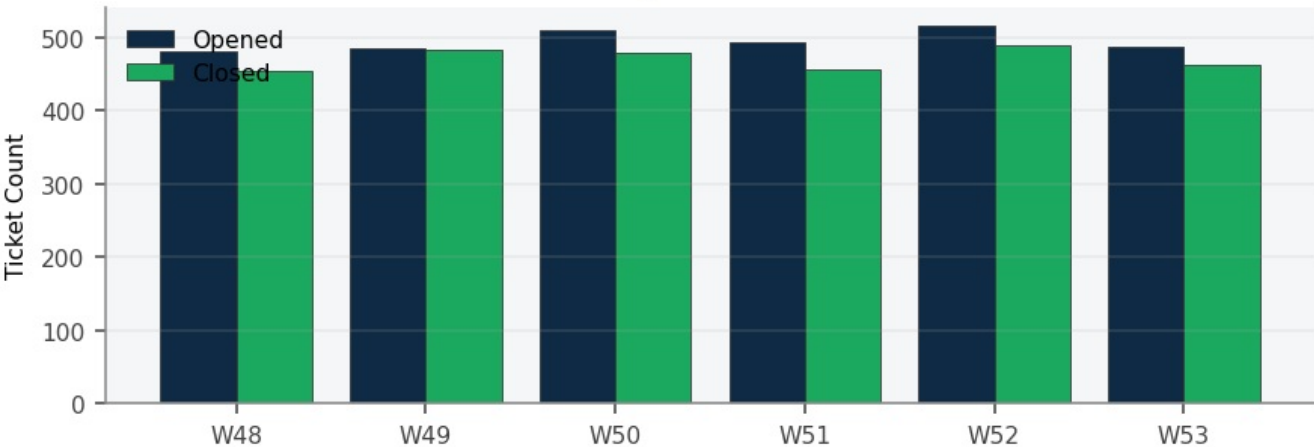


Figure 1. Ticket Volume — 6-Week Trailing

Tier 1 Avg Time to Acknowledge: 8m 14s
(Target ≤ 10 min)

Tier 2 Avg Time to Resolve: 4.7d
(Target ≤ 5.0 days)

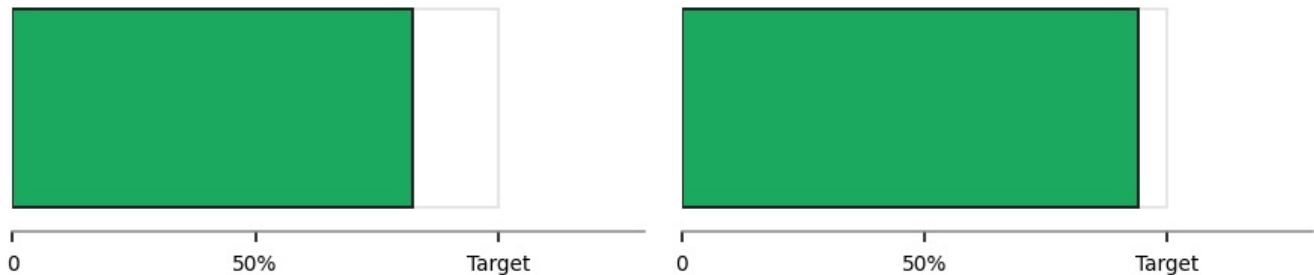


Figure 2. Tier 1 / Tier 2 SLA Performance vs. Targets

2. WORK ACCOMPLISHED

- Continued migration of NAS Pax River tenant accounts to consolidated identity platform. 86 accounts migrated this period; cumulative 1,247 of approximately 2,200 in scope.
- Patched and validated 318 endpoints on monthly cycle.
- Supported new arrival in-processing for 23 personnel.
- Met with Capt. Mark Walsh (Installation Operations) on 06 January 2026 regarding tenant command request for differentiated SLAs by tenant. Capt. Walsh indicated several tenant POCs have raised the request informally over Q4 FY25. Cardinal advised that PWS does not currently differentiate SLAs by tenant and any change requires COR direction.

3. ISSUES, RISKS, AND RFIS

- RFI-046 (submitted 09 January 2026): Following meeting with Capt. Walsh, request COR direction on whether to develop tiered SLA proposal for

tenant command differentiation. Status: Open.

Open RFIs from prior periods:

- RFI-041 (submitted 28 November 2025, OY1 Week 47): Clarification on PWS Section 4.1.2 — definition of "after-hours support" and whether 24/7 monitoring of NAVAIR-controlled subnet is in scope. **42 days open.**
- RFI-042 (submitted 11 December 2025, OY1 Week 49): Authority to procure replacement KVM hardware for tenant command operations center. 31 days open.
- RFI-044 (submitted 22 December 2025, OY1 Week 51): Clarification on PWS Section 5.4 — software deployment approval workflow when tenant command requests software not on standard image. 19 days open.

4. COST AND SCHEDULE PERFORMANCE (CUMULATIVE THROUGH 09 JANUARY 2026)

Metric	Value
BCWS (Cumulative)	\$5,142,000
BCWP (Cumulative)	\$5,063,000
ACWP (Cumulative)	\$5,478,000
CV (BCWP – ACWP)	-\$415,000
CV %	-8.2%
SV (BCWP – BCWS)	-\$79,000
SV %	-1.5%
EAC (Estimate at Completion)	\$6,890,000
EAC vs. CBB	\$190K over CBB at current trajectory

5. VARIANCE NARRATIVE (PNR-STYLE)

Cost variance has trended unfavorably since approximately OY1 Week 36 (mid-September 2025). Primary drivers identified by Cardinal:

- (a) Open-ended after-hours support requests against PWS Section 4.1.2 ambiguity (RFI-041) — Cardinal staff have responded to off-hours tenant requests on a "no-fault" basis pending COR direction, contributing approximately \$108K of unbudgeted labor over Q4 FY25.
- (b) Rework on software deployment package for tenant command "ENGAGE" platform (Q3 FY25) — Cardinal initially deployed package per verbal direction from Capt. Walsh's office in July; subsequent COR direction in September required reconfiguration to comply with installation security baseline. Rework cost: approximately \$87K. (See OY1 Weeks 28–34 reports for full chronology.)
- (c) Additional tier-2 support volume from tenant command growth not reflected in CPFF labor baseline.

6. PENDING ITEMS / GOVERNMENT ACTION REQUIRED

- Four (4) RFIs open. RFI-041 (42 days) is approaching escalation threshold per contract administration guidance.
- Cardinal recommends that COR convene a working session with affected tenant command POCs to resolve PWS Section 4.1.2 (after-hours scope) before further unbudgeted labor accrues.
